


DATE: 9/6/2012 Tb				DAILY WORKOVER / COMPLETION REPORT				ISO	
WELL NAME & NO.						FIELD			
UNIVERSITY F-10-I						TRIPLE N			
SEC.		TWP		RGE		COUNTY		STATE	
						ANDREWS		TX	
AFE NO.		W.I. 50%				GROSS AFE			
JOB DESCRIPTION:						SUPPLEMENT 1			
FISH PARTED RODS, PULL TUBING STRING, RUN BIT & SCRAPER AND CLEAN UP WELLBORE. RUN RRC H-15 MIT TEST.						TOTAL GROSS AFE			
REG		SIZE		WT.		GRADE		DEPTH	
C	S	8-5/8"		32#		K-55		1699'	
		5-1/2"		17#		K-55		4430'	
T	B								
		2-3/8"		4.70#		J-55		SRD	
PERFS:									
JOB#1138		TD		PBTD		PERFS		FORMATION	
		4430'		4375'		4308'-4316'		GRAYBURG	
COST ITEMS		\$		VENDOR		PKR/TAC		S.N. @	
						EOT @		ON-OFF	
RIG		3600		J&M -A		none		4145'	
BOPS		0		ST -B		WORK PERFORMED			
PUMP REPAIR		0		Andrews Pump -C		Start time: 7.00am Stop time: 5:30pm			
SUPERVISOR		1200		AMERICO -D		Held safety meeting with rig crew.			
BACK HOE		0		JRC -E		Opened well, flowing small stream of water.			
REVERSE UNIT		0		Weatherford -F		Continued Gih with 3/4" sucker rods. Slowed down and check each rod			
Vac Truck		0		TAJES -G		as going in the hole. Finished going in hole with 2"x1-1/2"x16" RXBC pump			
Pressure Recorder		600		BM. Vace -H		on 164-3/4" rods. (Laid down and replaced 21-3/4" rods with pits).			
AD-1 packer		300		Peak packer -I		Spaced out with 6' pony rod. Sealed pump and HWOB. Put well on pumping.			
Bolts/Nuts		90		Prod specialty -J		Test pump action, good. Will Rig Down Tomorrow.			
						tubing Landing:			
						132 joints 2-3/8" EUE Red J-55 tubing			
						at 4145'			
						2-3/8" Seating Nipple			
						Perforated sub			
						2 joints of mud anchor			
						Bull plug.			
						4213'			
						2"x1-1/2"x16 ft RXBC			
						164-3/4" rods			
						6' pony rod			
						Polished rod			
DAILY COST		5,790				ACCIDENTS: -0-			
CCOST		29,460				REPORTED BY: HADI			
TOTAL COST		35,250		835,250		RIG# J&M		PHONE: 361-649-7340	

VENDOR	\$-DAILY COST	\$-CC.COST
A-J&M	3600	18700 service rig
B-ST	0	400 BOP rent
C-Andrew pump	0	500 repair pump,collars, dope
D-Americo	1200	6000 supervisor
E-JRC	0	450 backhoe operation
F-weatherford	0	6200 reverse unit
G-Tajes vac	0	950 hauled water to pit
H-BM vac	600	900 provide recorder chart.
I-Peak	300	1000 Rented AD-1 packer
J-Prod specialty	90	150 wellhead bolts & nuts,gas anchor,pony rods

DALY COST: \$5,790

CC.COST : \$35,250

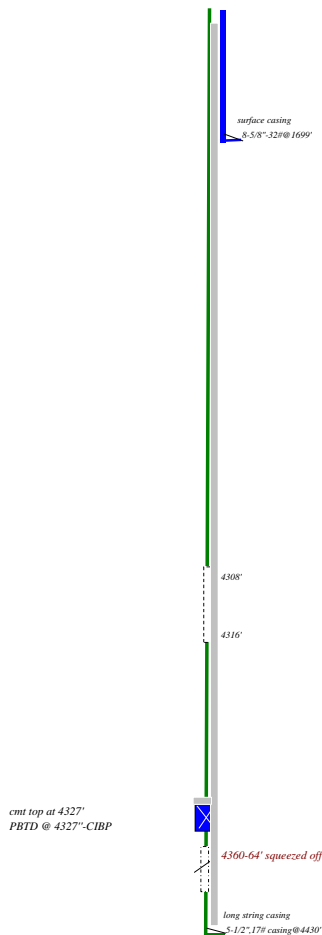

TD: drilled 4430'
Hadi
