


DATE: 9/7/2012    Frid		DAILY WORKOVER / COMPLETION REPORT				ISO	
WELL NAME & NO.				FIELD			
UNIVERSITY    F-10-I				TRIPLE N			
SEC.		TWP		RGE		COUNTY	STATE
						ANDREWS	TX
AFE NO.		W.L. 50%				GROSS AFE	
JOB DESCRIPTION:				SUPPLEMENT 1			
FISH PARTED RODS, PULL TUBING STRING, RUN BIT & SCRAPER AND CLEAN UP WELLBORE. RUN RRC H-45 MIT TEST.				TOTAL GROSS AFE			
		SIZE		WT.		GRADE	
C		8-5/8"		32#		K-55	
S		5-1/2"		17#		K-55	
G							
T		2-3/8"		4.70#		J-55	
B						SRD	
G							
PERFS:				TD		PBTD	
JOB#1138				4430'		4375'	
				4308'-4316'		FORMATION	
				GRAYBURG			
COST ITEMS		\$		VENDOR		PKR/TAC	
RIG		2200		J&M		S.N. @	
BOPS		0		ST		EOT @	
PUMP REPAIR		0		Andrews Pump		4145'	
SUPERVISOR		1200		AMERICO		4213'	
BACK HOE		0		JRC			
REVERSE UNIT		0		Weatherford			
Vac Truck		0		TAJES			
Pressure Record		0		BM. Vace			
AD-1 packer		0		Peak packer			
Bolts/Nuts		0		Prod specialty			

VENDOR	\$-DAILY COST	\$-CC.COST
A-J&M	2200	20900 service rig
B-ST	0	400 BOP rent
C-Andrew pump	0	500 repair pump,collars, dope
D-Americo	1200	7200 supervisor
E-JRC	0	450 backhoe operation
F-weatherford	0	6200 reverse unit
G-Tajes vac	0	950 hauled water to pit
H-BM vac	0	900 provide recorder chart.
I-Peak	0	1000 Rented AD-1 packer
J-Prod specialty	0	150 wellhead bolts & nuts,gas anchor,pony rods

DALY COST: \$3,400

CC.COST : \$38,650

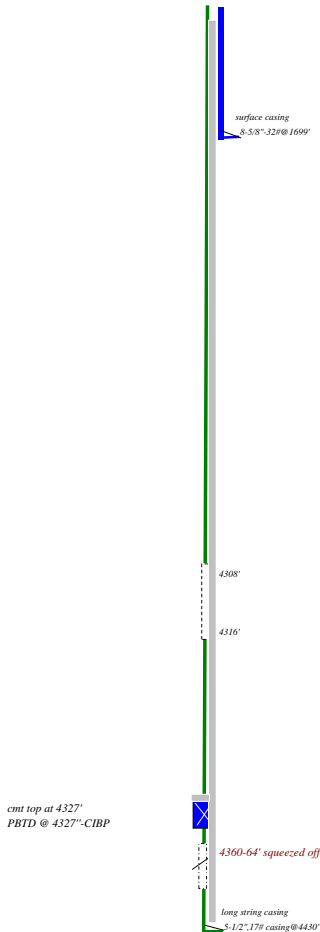

TD: drilled 4430'  
Hadi
